

Building the SOFSA C-ICP



Randy Molten, Lt Col
HQ USSOCOM/SOAL-L
DSN 299-8898

Outline



- SOFSA Info
- SOFSA Vision
- SOFSA Core Capabilities
- C-ICP Vision
- Building a Team
- Building the C-ICP
- Lessons Learned - *so far*

SOF Support Activity



- What is SOFSA?
 - HQ USSOCOM contract with L-3 Communications
 - Ten year (max) Indefinite Delivery-Indefinite Quantity, Cost Reimbursable, Plus Award Fee contract
 - Awarded Apr 2003; \$1.5B ceiling
 - Available for use throughout USSOCOM including PEOs and Components
 - Dedicated logistics support to Joint SOF
 - Leased facilities; on-site Government Staff

SOFSA Provides...




- A dynamic partnership between USSOCOM, components, DoD, and industry
- The “Cornerstone” for executing USSOCOM’s SO-peculiar logistics (repair, maintenance, modifications and sustainment)
- “Center of Excellence” for SOF aviation modifications
- Broad and flexible Performance-Based Statement of Work
 - Responsiveness to time sensitive requirements
 - Priority to Joint SOF
- USSOCOM Logistics Operators

SOFSA Background




- Why SOFSA?
 - USSOCOM acquisition authority—HDLD assets
 - SOFSA #1 priority is USSOCOM & SOF
 - Capability to support joint SOF requirements
 - ***Provides SO-peculiar equipment, materials, supplies and services***

Organization

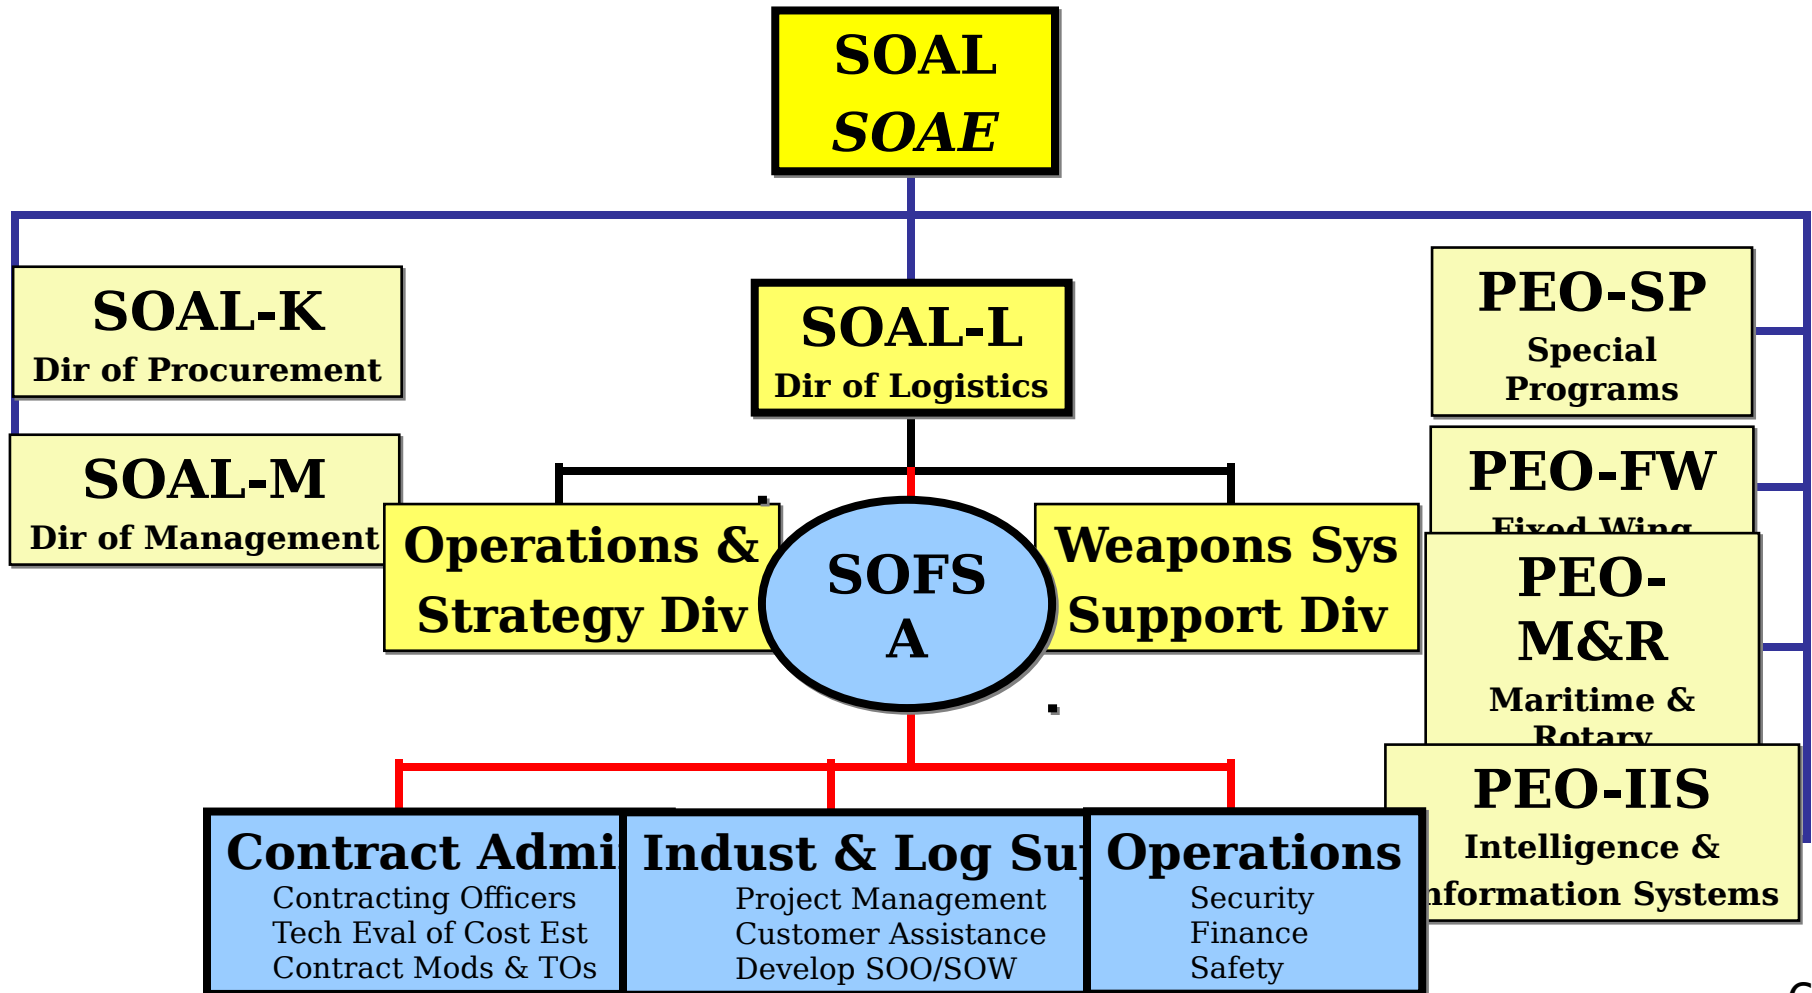


SOFSA Core Capabilities

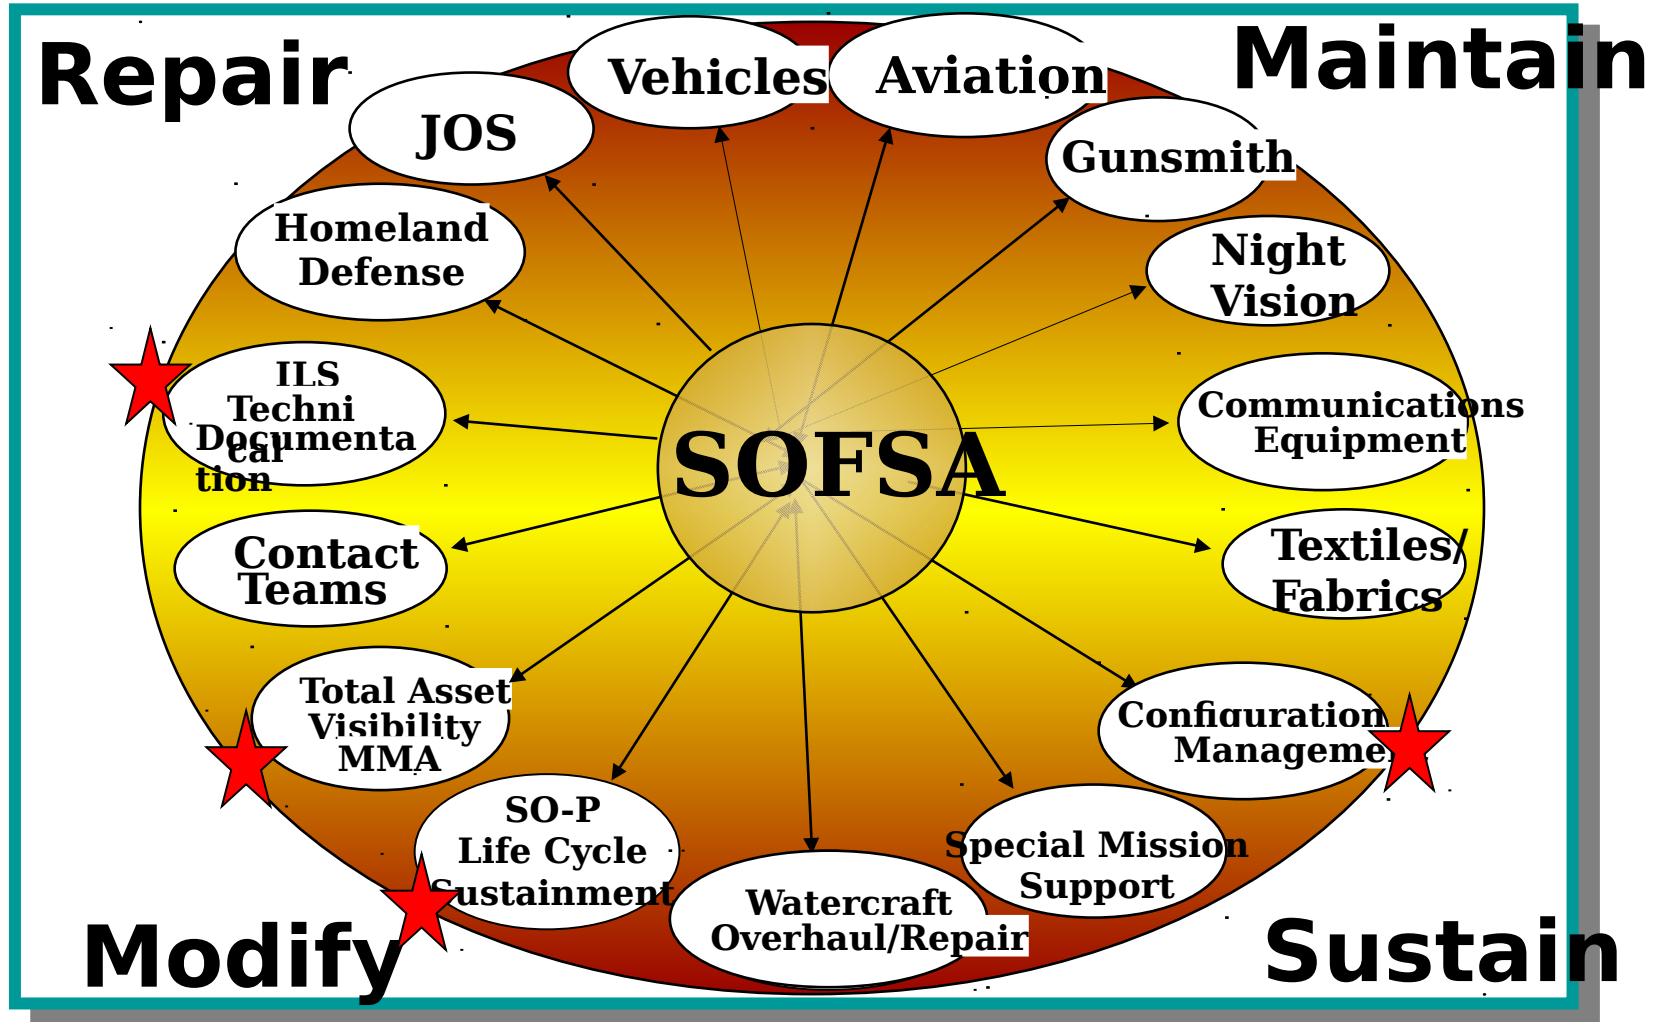

C-ICP Vision for SOFSA

- One team supporting SO-P asset life cycle sustainment requirements
- One team determining future supportability needs
- One team managing configuration control

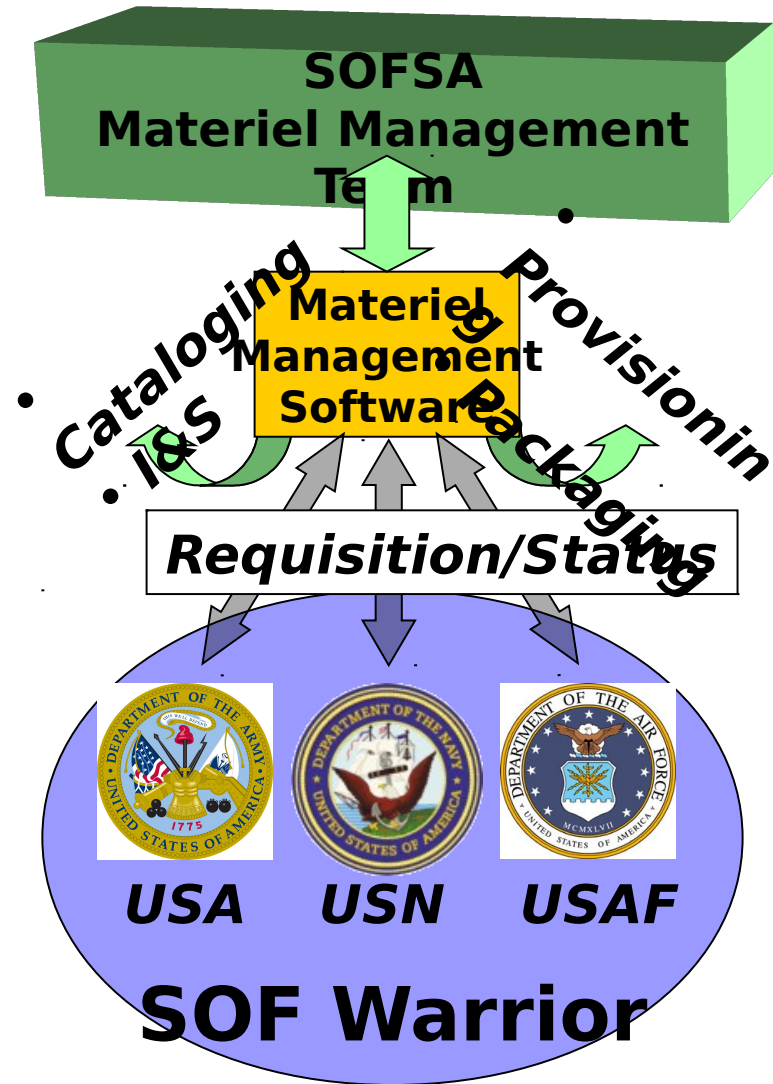

Existing C-ICP Candidates

- SO-Peculiar assets currently managed at SOFSA in a non-ICP environment will populate
 - **Forward Area Manifold (FAM) Cart**



Using the CSWS Guide




- Great tool
- We're just a little bit different...
 - Contract in place, 600+ task orders
 - CSWS application is for many systems, not just one airframe
 - We don't anticipate many NSN transitions
 - We're making this joint
 - Still not sure if this'll be easy, ~~hard, or impossible~~

Completed Activities To Date



- Sep 03 - SOFSA approved as CSWS candidate
 - HQ AFMC starts assigning C-ICP codes
- Nov 03 - USN, USA discussions initiated
 - C-ICP project risk assessment report completed
- Dec 03 - SOAE informed of C-ICP activities
 - GOLD selected as Materiel Mgmt System
 - SSIPT announcement/e-mail distributed
- Jan 03 - SPIRENT on contract; H/W, S/W on order
 - C-ICP 'joint issues' under review, in discussion
 - SOFSA building ICP Cell, hiring talent
- Feb 03 - SPIRENT site survey conducted at SOFSA
 - Data Exchange training

Material Management System



- GOLD MMS selected for C-ICP functionality
- Unique GOLD utilization
 - GOLD functions will replace 4 existing SOFSA legacy systems/functions—requires advanced integration with SOFSA MIS operations
 - Supply mgmt, calibration, property control, and equip mgmt
- SPIRENT has conducted site survey at SOFSA; is preparing implementation plan and schedule


The Road Ahead



- Merge SPIRENT, L3Com, and AFMC/SOCOM schedules into one integrated plan
 - Shooting for a Fall '04 turn-on
- SOFSA identifying initial SO-P candidates
 - Catalog actions, etc.
- Installing H/W, S/W
- Training preparations (AFMC)
- Testing 'jointness'
 - SARS, UADPS, SBSS

Known Unknowns

- Issue: How should we catalog multi-service used, contractor managed weapon systems/assets?
 - AFMC Proposal: Create and implement a new MOE Code for a contractor-managed weapon system
- Issue: What tools can our SOFSA Contractor use in lieu of Data Exchange (for non-USAF assets)?

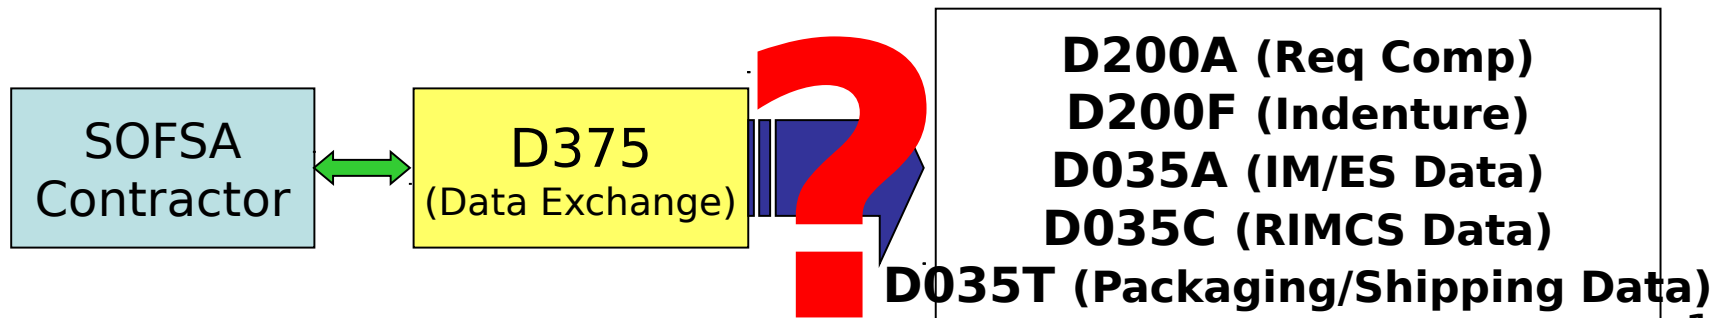

Bottom Line

- SOCOM gladly accepts any/all technical/logistical assistance with making this effort...
 - A reality
 - As smooth as possible
 - A timely one
- We have demanding customers

